

Cliente Exemplo S.A.

Roadmap de Transformação em IA

Parte 2: DevOps Lifecycle


ASSESSMENT	AI Maturity Assessment 2026 H1
INDÚSTRIA	Financial Services / Insurance
DATA DO ASSESSMENT	2026-05-08
VERSÃO DO FRAMEWORK	1.0.0
GERADO EM	2026-05-08
ESCOPO	Engineering Organization

Sumário

1. Resumo Executivo	.
2. Roadmap de Transformação	.
2.1 Horizonte 1: Fundação (Meses 0-6)	.
2.2 Horizonte 2: Escala (Meses 6-18)	.
2.3 Horizonte 3: Transformação (Meses 18-36)	.
3. Recursos	.
4. Métricas de Sucesso	.
5. Riscos e Mitigações	.
6. Próximos Passos Recomendados	.

1. Resumo Executivo

Este documento apresenta o roadmap de transformação para DevOps Lifecycle como parte da jornada de AI-Native Software Delivery Maturity de Cliente Exemplo S.A.. O roadmap delinea as iniciativas estratégicas, esforço e cronograma necessários para evoluir da maturidade atual do pilar (L1.5) ao nível-alvo (L4.0) ao longo de um período de 36 meses.

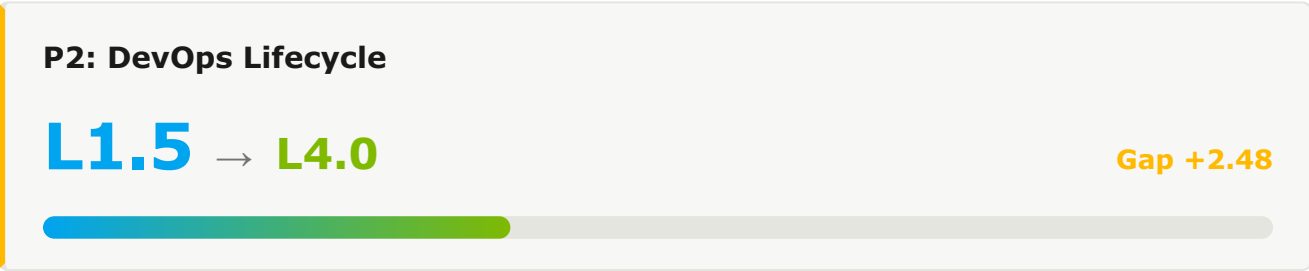

1.1 Avaliação do Estado Atual

MÉTRICA	VALOR ATUAL	VALOR ALVO	GAP
Deployment Frequency	Weekly	On-demand	Daily → On-demand
Lead Time for Changes	1-7 days	<1 hour	Significant
Change Failure Rate	15%	<5%	+10pp

1.2 Pontuações de Capabilities do Pilar 2

#	CAPABILITY	ATUAL	META	GAP	PRIORIDADE
2.1	Source Control & Branching Strategy	L2.3	L3.0	0.7	(PRIORITY.P3)
2.2	PE CI/CD Pipelines	L0.0	L3.0	0.0	(PRIORITY.P3)
2.3	Build & Artifact Management	L2.4	L3.0	0.6	(PRIORITY.P3)
2.4	Test Automation	L0.8	L3.5	2.8	(PRIORITY.P0)
2.5	PE Security & DevSecOps	L0.0	L3.0	0.0	(PRIORITY.P3)
2.6	Release & Deployment Strategy	L0.0	L3.0	0.0	(PRIORITY.P3)
2.7	PE Observability & Monitoring	L0.0	L3.0	0.0	(PRIORITY.P3)
2.8	Incident Management & SRE	L0.0	L3.0	0.0	(PRIORITY.P3)
2.9	Chaos Engineering	L0.0	L3.0	0.0	(PRIORITY.P3)
2.10	Compliance & Audit Automation	L0.7	L3.0	2.3	(PRIORITY.P0)

2. Roadmap de Transformação

A transformação se desdobra em três horizontes temporais — H1 (Fundação, Meses 0-6), H2 (Escala, Meses 6-18) e H3 (Transformação, Meses 18-36) — permitindo construção progressiva de capabilities enquanto entrega valor incremental em cada etapa.

2.1 Horizonte 1: Fundação (Meses 0-6)

Meta: L1.5 → L2.5 · Establishing AI-Assisted Development Foundation

2.1 Source Control & Branching Strategy

Atual: L2.3 → Meta H1: L2.5 · Gap: 0.2

EVIDÊNCIAS DO ESTADO ATUAL

- Mixed branching strategies
- Partial signed-commit enforcement

INICIATIVAS H1

- ✓ Standardize on trunk-based development
- ✓ Enforce branch protection org-wide
- ✓ Mandate signed commits across all repos

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
Trunk-based Repos	40%	85%

PE 2.2 CI/CD Pipelines

Atual: L0.0 → Meta H1: **L2.5** · Gap: 2.5

EVIDÊNCIAS DO ESTADO ATUAL

- 60% CD coverage
- Manual prod gates

INICIATIVAS H1

- ✓ Achieve 100% CD pipeline coverage
- ✓ Replace manual gates with automated checks
- ✓ Implement progressive delivery patterns

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
CD Coverage	60%	85%

2.3 Build & Artifact Management

Atual: L2.4 → Meta H1: **L2.5** · Gap: 0.1

EVIDÊNCIAS DO ESTADO ATUAL

- 50% SBOM coverage
- No reproducibility enforcement

INICIATIVAS H1

- ✓ Achieve 100% SBOM coverage
- ✓ Mandate reproducible builds
- ✓ Optimize build cache hit rates

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
SBOM Coverage	50%	100%

2.4 Test Automation

Atual: L0.8 → Meta H1: **L2.5** · Gap: 1.8

EVIDÊNCIAS DO ESTADO ATUAL

- 100% unit, 70% integration
- Manual flaky-test triage

INICIATIVAS H1

- ✓ Deploy automated flaky-test detection
- ✓ Move E2E tests to PR pipeline for critical paths
- ✓ Standardize test parallelization

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
Integration Coverage	70%	90%

PE 2.5 Security & DevSecOps

Atual: L0.0 → Meta H1: **L3.0** · Gap: 3.0

EVIDÊNCIAS DO ESTADO ATUAL

- 100% SAST/SCA
- 60% DAST
- Threat modeling pilot

INICIATIVAS H1

- ✓ Expand DAST to 100% of public services
- ✓ Roll out threat modeling tool org-wide
- ✓ Integrate AI vulnerability prioritization

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
DAST Coverage	60%	100%

2.6 Release & Deployment Strategy

Atual: L0.0 → Meta H1: **L2.5** · Gap: 2.5

EVIDÊNCIAS DO ESTADO ATUAL

- 30% canary
- 40% feature flags

INICIATIVAS H1

- ✓ Standardize feature flags across all services
- ✓ Expand canary deployments to 80% of services
- ✓ Automate rollback decisions based on SLO breaches

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
Canary Coverage	30%	70%

PE 2.7 Observability & Monitoring

Atual: L0.0 → Meta H1: **L3.0** · Gap: 3.0

EVIDÊNCIAS DO ESTADO ATUAL

- 80% tracing
- 70% SLOs
- Manual alerting

INICIATIVAS H1

- ✓ Deploy AI-driven anomaly detection
- ✓ Achieve 100% SLO coverage
- ✓ Reduce alert noise via intelligent grouping

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
SLO Coverage	70%	100%

2.8 Incident Management & SRE

Atual: L0.0 → Meta H1: **L2.0** · Gap: 2.0

EVIDÊNCIAS DO ESTADO ATUAL

- MTTR 30min-8h
- No SRE practice

INICIATIVAS H1

- ✓ Establish formal SRE function
- ✓ Standardize postmortem and action-item tracking
- ✓ Deploy AI-assisted incident triage

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
MTTR (P95)	8h	2h

2.9 Chaos Engineering

Atual: L0.0 → Meta H1: **L1.5** · Gap: 1.5

EVIDÊNCIAS DO ESTADO ATUAL

- No chaos practice
- Annual DR only

INICIATIVAS H1

- ✓ Deploy chaos engineering tooling
- ✓ Establish quarterly game day cadence
- ✓ Build chaos testing into pre-prod pipelines

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
Game Days/yr	0	4

2.10 Compliance & Audit Automation

Atual: L0.7 → Meta H1: **L2.5** · Gap: 1.8

EVIDÊNCIAS DO ESTADO ATUAL

- 80% audit trail
- Partial compliance automation

INICIATIVAS H1

- ✓ Automate evidence collection for all controls
- ✓ Deploy continuous compliance dashboards
- ✓ Integrate compliance checks into CD pipelines

MÉTRICAS DE SUCESSO

MÉTRICA	ATUAL	META H1
Automated Controls	60%	85%

2.2 Horizonte 2: Escala (Meses 6-18)

Meta: **L2.5** → **L3.0** · Scaling Platform Engineering & Agentic Workflows

Iniciativas Principais

IDP GENERAL AVAILABILITY

- ✓ Migrate all teams to IDP
- ✓ Establish golden paths for top 10 use cases
- ✓ Deploy AI-enhanced developer self-service

AGENTIC WORKFLOWS

- ✓ Roll out Agent Mode org-wide
- ✓ Deploy AI-driven pipeline optimization
- ✓ Implement AI test selection and prioritization

Metas de Capabilities — H2

CAPABILITY	SAÍDA H1	META H2	HABILITADOR-CHAVE
2.1 Source Control & Branching Strategy	L2.5	L3.5	AI-based PR routing
2.2 CI/CD Pipelines	L2.5	L3.5	AI-driven pipeline optimization
2.3 Build & Artifact Management	L2.5	L3.5	Distributed remote caching
2.4 Test Automation	L2.5	L3.5	AI test selection
2.5 Security & DevSecOps	L3.0	L3.5	AI-driven runtime protection
2.6 Release & Deployment Strategy	L2.5	L3.5	AI-driven release decisions
2.7 Observability & Monitoring	L3.0	L3.5	AI anomaly detection org-wide
2.8 Incident Management & SRE	L2.0	L3.0	AI-driven incident response
2.9 Chaos Engineering	L1.5	L2.5	Production chaos experiments
2.10 Compliance & Audit Automation	L2.5	L3.5	AI control attestation

2.3 Horizonte 3: Transformação (Meses 18-36)

Meta: L3.0 → L4.0 · Autonomous Operations and Self-Healing Systems

Iniciativas Principais

AUTONOMOUS SDLC

- ✓ Deploy multi-agent coding workflows
- ✓ Implement autonomous progressive delivery
- ✓ Achieve self-healing infrastructure

CONTINUOUS OPTIMIZATION

- ✓ AI-driven workload placement
- ✓ Predictive incident prevention
- ✓ Continuous compliance with AI verification

Metas de Capabilities — H3

CAPABILITY	SAÍDA H2	META H3
2.1 Source Control & Branching Strategy	L3.5	L4.0 — Continuous integration with AI gating
2.2 CI/CD Pipelines	L3.5	L4.0 — Self-healing pipelines
2.3 Build & Artifact Management	L3.5	L4.0 — Hermetic builds with provenance
2.4 Test Automation	L3.5	L4.0 — Predictive test orchestration
2.5 Security & DevSecOps	L3.5	L4.0 — Autonomous security response
2.6 Release & Deployment Strategy	L3.5	L4.0 — Autonomous progressive delivery
2.7 Observability & Monitoring	L3.5	L4.0 — Predictive incident prevention
2.8 Incident Management & SRE	L3.0	L4.0 — Self-healing systems
2.9 Chaos Engineering	L2.5	L4.0 — Continuous chaos with AI safety net
2.10 Compliance & Audit Automation	L3.5	L4.0 — Continuous compliance with AI verification

3. Recursos

3.1 Investimentos em Tecnologia

As tecnologias abaixo são recomendadas ao longo do roadmap de 36 meses. O nível de esforço indica o custo de implementação de cada uma — veja legenda abaixo.

TECNOLOGIA	HORIZONTE	ESFORÇO	PROPÓSITO
Progressive Delivery Platform	H1	M	Canary + feature flags org-wide
AI Anomaly Detection	H1	M	Observability augmentation
Chaos Engineering Tooling	H2	S	Resilience validation
AI Pipeline Optimization	H2	M	Build/test/deploy intelligence
Self-Healing Pipelines	H3	L	Autonomous CI/CD

3.2 Time e Skills

PAPEL	FTES	HORIZONTE	FOCO
Platform Engineering Lead	1	H1	Pipeline strategy
SRE Engineers	4	H1	SRE function buildout
Security Engineers	2	H1	DevSecOps deepening
Platform Engineers	6	H2	Observability & chaos engineering

3.3 Resumo de Esforço por Horizonte

HORIZONTE	DURAÇÃO	ESFORÇO	ÁREAS DE FOCO
H1	0-6 months	M	Progressive delivery, SRE foundation
H2	6-18 months	L	Chaos eng, AI pipelines
H3	18-36 months	L	Self-healing operations
TOTAL	36 meses	L	Transformação completa do DevOps Lifecycle

LEGENDA DE NÍVEL DE ESFORÇO

S	M	L	XL
Pequeno 4-8 semanas · 2-3 FTE · 1 squad	Médio 2-4 meses · 4-6 FTE · 1-2 squads	Grande 4-9 meses · 7-12 FTE · 2-3 squads	Extra-Grande 9+ meses · 12+ FTE · cross-org

4. Métricas de Sucesso

4.1 Evolução das Métricas DORA

MÉTRICA	ATUAL	META H1	META H2	META H3
Deployment Frequency	Weekly	Daily	Multi-daily	On-demand
Lead Time for Changes	1-7 days	<1 day	<4 hours	<1 hour
Change Failure Rate	15%	10%	7%	<5%
MTTR (P95)	8h	4h	1h	<30 min

4.2 Métricas Operacionais

MÉTRICA	ATUAL	META H1	META H2	META H3
SLO Coverage	70%	100%	100%	100%
Game Days/yr	0	4	12	Continuous
Incident MTTR	8h	2h	30min	<10min auto

5. Riscos e Mitigações

RISCO	IMPACTO	PROBABILIDADE	MITIGAÇÃO
Pipeline disruption during transition	ALTA	BAIXA	Staged rollout, parallel pipelines, automated rollback
Security regression with AI tooling	ALTA	BAIXA	AI-aware security scanning, mandatory review, audit trails
Tool sprawl	MÉDIA	MÉDIA	Standardize on validated tool catalog, sunset legacy tools per quarter

6. Próximos Passos Recomendados

6.1 Ações Imediatas (Próximos 30 Dias)

- 1 Establish formal SRE function with named lead
- 2 Inventory existing pipeline maturity per service
- 3 Identify priority services for canary + feature flag rollout
- 4 Define SLO target framework
- 5 Procure progressive delivery tooling

6.2 Atividades de Lançamento H1 (Dias 30-90)

- 1 Achieve 100% CI/CD pipeline coverage gap closure for prioritized services
- 2 Deploy AI anomaly detection to first 5 tier-1 services
- 3 Run first chaos engineering game day
- 4 Standardize postmortem template and tracking
- 5 Launch DevSecOps deepening initiative (DAST 100%, threat modeling)

6.3 Dependências

- Part 1: Developer Productivity for AI test generation alignment
- Part 3: Application Platform observability stack alignment
